

JULY 2023

**KAREE TAILINGS
 STORAGE FACILITY (TSF) 4**

DETAILS OF TAILINGS STORAGE FACILITY

Tailings Storage Facility (TSF) Name	Karee Mine K4 Concentrator TSF 4
Operation	Marikana
Operational Status	Active
Operating Segment	RSA - PGM
Location	45km east of the town of Rustenburg in the North West province - please refer to Figure 1
Latitude, Longitude (decimals)	-25.6498, 27.4491
Ore Source	Underground
Type of Storage Facility	Impoundment (upstream development)
Deposition Methodology	Spigot, converting to Hybrid Paddock System during 2023
Year of Commissioning	2008
Consequence Classification (GISTM, 2020)	Very High
Operating Contractor	Fraser Alexander (Pty) Ltd (FAT)
Engineer of Record (EoR)	SLR Consulting (Pty) Ltd
Current Maximum Height (m)	17
Final Maximum Height (m)	36
Maximum Storage Capacity (tons/month)	220 000
Total Volume Already Deposited (Mm³)	9.6
Life of TSF (year)	2045 @1.3m/yr, 2043 @1.5m/yr



INNOVATION



COMMITMENT



ACCOUNTABILITY



RESPECT



ENABLING



SAFETY

TECHNICAL ASPECTS:

Design Criteria

GISTM and best practice guidelines including Australian National Committee on Large Dams (ANCOLD) (Guidelines on Tailings Dams, July 2019). Site specific design criteria were specified by the EoR. Details are included in the Design Basis Report (DBR).

Stability Assessment and Mitigation Measures

A detailed stability assessment based on piezocone probing and laboratory test work was conducted in 2022. (SLR Project No: 720.19129.00042 Rev 0, 28 February 2023)

All the FoS are above the required legal limits and thus no mitigation measures were required

Dam Breach Assessment

Assessment completed in 2022
 (SLR Project No: 720.19129.00011 Rev 1, February 2023)

Area of Inundation

Has been identified by EoRs – please refer to Figure 2

Summary of Human Exposure

Consequence classification has been based on Population at Risk (PAR). Communities have been identified and are being engaged through various means including Community Engagement Forums (CEF)

DOCUMENTATION:

Site Specific OMS Manual

Version 2022 available

Mandatory Code of Practice (MCOP) Document No: SS-ZA-PGM's-MCOP-CON-TLS-0101 is in place (dated September 2022)

Design Basis Report (DBR)

Version 2022 available
 (SLR Project No: 720.19129.00033 Rev 1, February 2023)

Environmental Management System

The Environmental Management System is ISO accredited (ISO 14001:2015)

The initial Environmental Management Programme (EMPr) is dated 2014.



INNOVATION



COMMITMENT



ACCOUNTABILITY



RESPECT



ENABLING



SAFETY

Surveillance:

Surveillance Frequency

Daily by the Operator and monthly reports of critical controls submitted to and reviewed by the EoR

Surveillance Technology/System

K2Fly Decipher

Deformation Monitoring

Interferometric Synthetic Aperture Radar (InSAR)

Phreatic Surface Levels & Pore Pressure Measurements

Standpipe piezometers
 AquaSense Retrofit piezometers (IoT device)

**RISK MANAGEMENT /
 EMERGENCY PREPAREDNESS:**

Risk Assessment

Annual Risk Assessment (Bowtie) completed with no untoward risk identified

Risk Management

Site specific OMS Manual in place
 Site specific Trigger Action Response Plans (TARPs) in place
 Critical controls established and implemented
 Operating contractor Technical and Operational Risk Assessment System (TORAS)

Site Specific Emergency Preparedness & Response Plans (EPRP)

Version 2023 available

Annual emergency mock drill for a catastrophic TSF failure – undertaken on 15 June 2023 with SSW employees and contractors.

Environmental emergency preparedness is managed on site according to ISO14001: 2015.

CLOSURE & POST CLOSURE

Closure Planning

In place - report prepared by Golder Associates (Golder Reference: 20141966-340280-9, June 2021)

Closure Costing

Adequate financial capacity in place
 Financials prepared by Golder Associates (Golder Reference: 21467970-349390-1, December 2021)

Asset Insurance Cover

In place – July 2022 to June 2023 (currently undergoing renewal)



INNOVATION



COMMITMENT



ACCOUNTABILITY



RESPECT



ENABLING



SAFETY

Independent Reviews:

Independent Tailings Review Board (ITRB)

12 July 2022 with no material concerns identified

Future ITRB Review

2025

Performance Reviews

Annual and quarterly reports and inspections completed by EoR
(SLR Project No: 720.19129.00033 Rev 0, March 2023)

Dam Safety Review (DSR)

Carried out by an independent third party in 2020. All recommendations at the time have been addressed in the last 2 years.
(KP Reference: RI301-00877/02 Rev B, 26 August 2022)

Next review scheduled for 2025



INNOVATION



COMMITMENT



ACCOUNTABILITY



RESPECT



ENABLING



SAFETY



Figure 1: Layout of Karee Tailings Dam Complex



INNOVATION



COMMITMENT



ACCOUNTABILITY



RESPECT



ENABLING



SAFETY

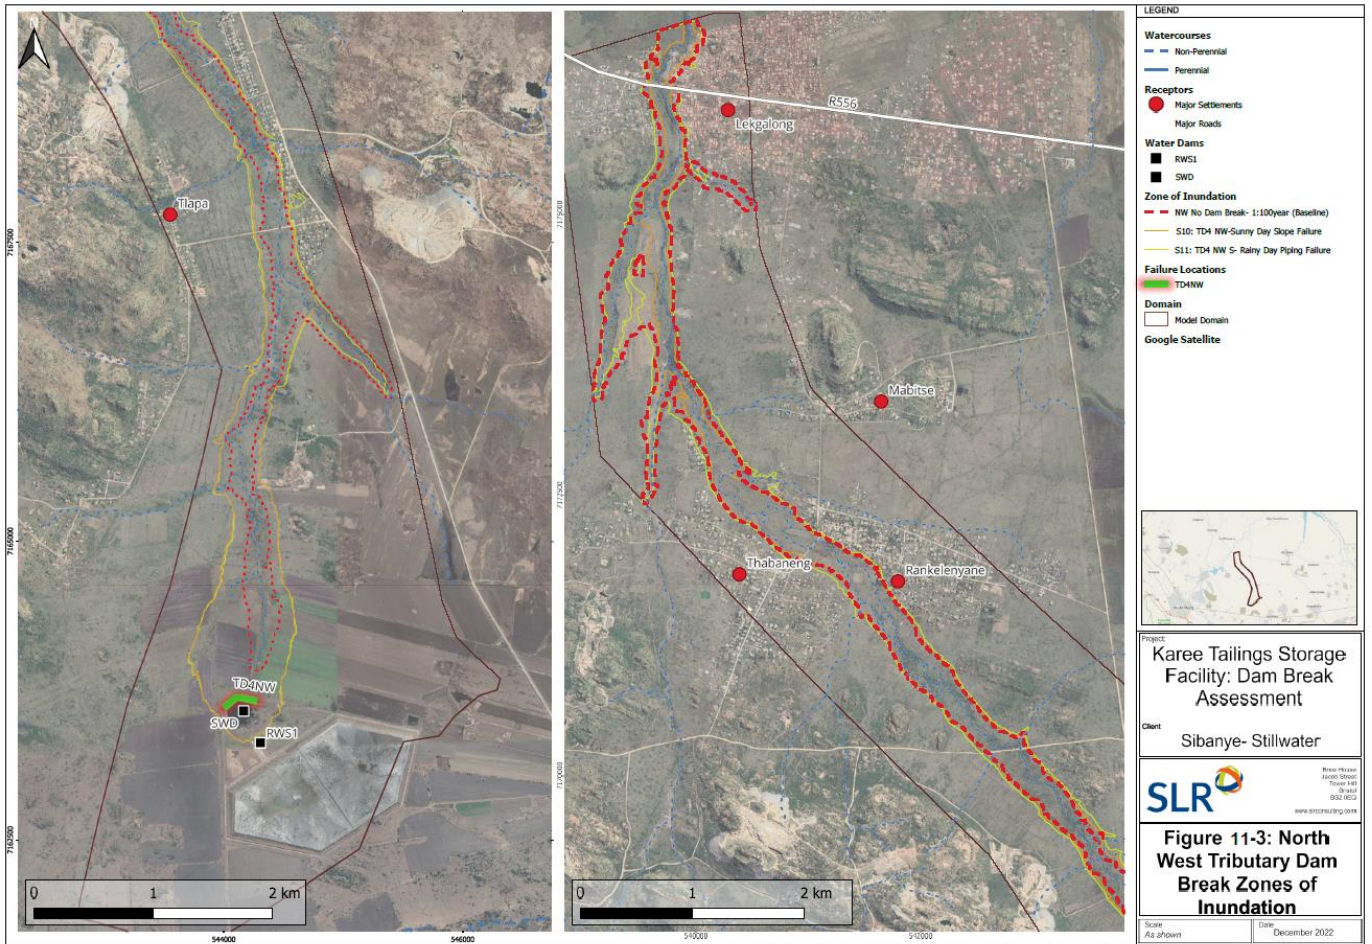


Figure 2: Area of Inundation (North-West tributary)
